



Burnhamthorpe Water Project

What's New?

March - April 2022 Residents' update: Burnhamthorpe and Central Parkway site

Hello neighbours: This is our latest bi-monthly update on the progress of the work at our site across the street.

Work completed so far:

- | | |
|---|-----------------------|
| 1. Site setup and utility relocations | Completed fall 2019 |
| 2. Shaft excavation | Completed winter 2020 |
| 3. Tunnel mining and watermain pipe installation | Completed summer 2020 |
| 4. Chamber outer wall construction | Completed fall 2020 |
| 5. Chamber interior walls, structures, roof support beams and panels | Completed spring 2021 |
| 6. Watermain Grouting | Completed spring 2021 |
| 7. Install chamber interior steel structures and watermain pipe components | Completed summer 2021 |
| 8. Putting watermain in service & connections | Completed fall 2021 |
| 9. Install roof support beams, panels, and topping slab | Completed fall 2021 |
| 10. Removal shaft support system, chamber backfill, site grading & removals | Completed winter 2021 |

Upcoming activities:

1. Site restoration activities


We anticipate our work will be done by mid 2022. Your patience is appreciated as we build the necessary water infrastructure to support Mississauga's growing downtown core.



Removal Shaft Support Systems



Chamber Backfill & Grading

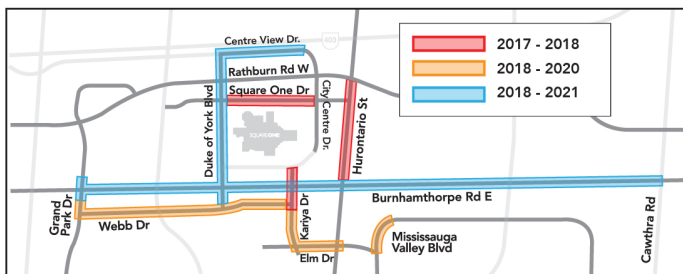

Project information:

- peelregion.ca/bwp
- bwp@peelregion.ca
- [@peelpublicworks](https://twitter.com/peelpublicworks)
- [#peelbwp](https://twitter.com/peelbwp)

Contact information:

Avalon Myers
Project Ambassador
416-457-3889

Heather Jefferson
Project Manager
905-791-7800, ext. 7881
